ARYADI BUSINESS PVT.LTD.

DAILY PROGRESS REPORT


PROJECT STATUS SUMMARY

ISO 9001:2015 | ISO 14001:2015 | ISO 45001:2018 Certified

TICKET NO	PROJECT START	PROJECT END	OVERALL PROGRESS
CS-PROJECT-062682	**2026-07-12**	**2026-07-14**	**100%**

Site Details		Project Details	
Branch Name	SIFY - Mumbai	**Project Name**	SIFY-MUMBAI-520261200645
Address	Sify Infinit Spaces Limited Plot No. R-847, 1/2, T.T.C. Industrial Area, MIDC Industrial Area, Sector 2, Rabale, Navi Mumbai, Maharashtra 400701	**Type**	Projects
		Ticket No	CS-PROJECT-062682
Mobile No.	9930287842	**Client Ticket Number**	—
		Project Start Date	2026-07-12
		Project End Date	2026-07-14

Overall Project Progress




OVERALL COMPLETION

100%

- Completed (100%)
- Pending (0%)

System Generated Report | Private & Confidential | Generated on: 01-Oct-2026 15:16

Task Progress Chart

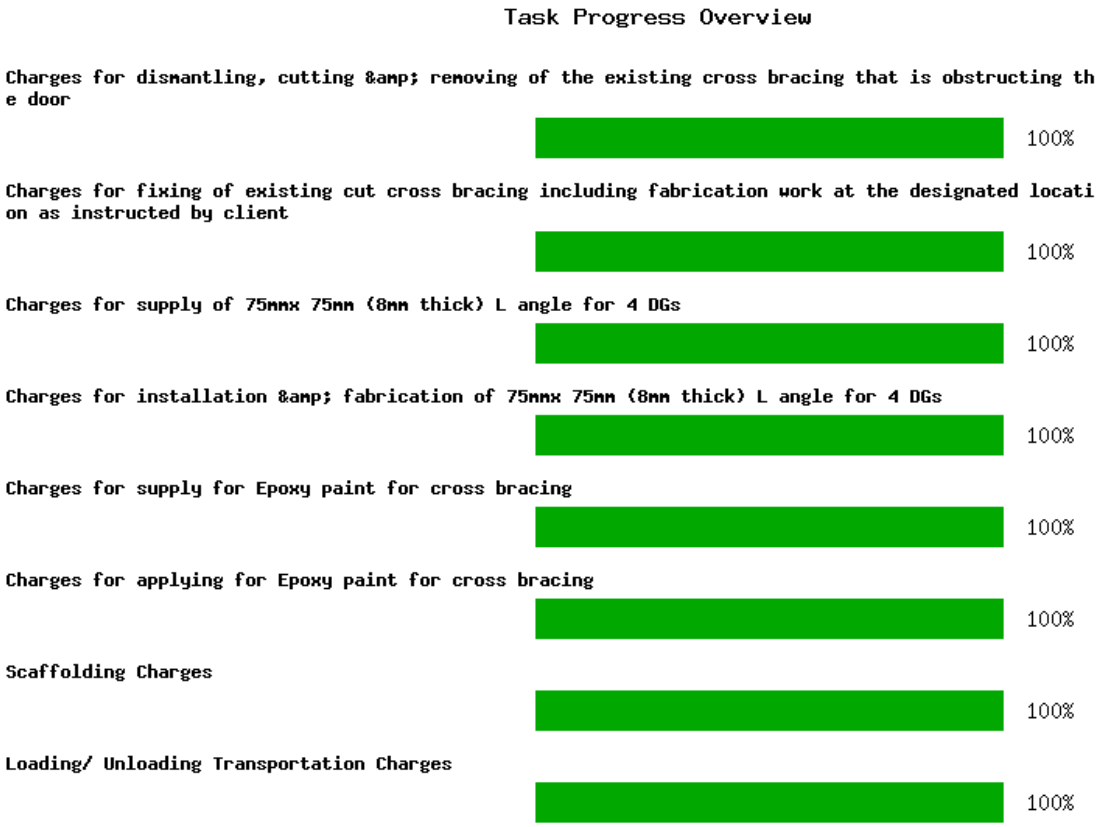

Project Task Timeline

TASK NAME	12-JUL	13-JUL	14-JUL	TOTAL
Charges for dismantling, cutting & removing of the existing cross bracing that is obstructing the door	100 %	0 %	0 %	100%
Charges for fixing of existing cut cross bracing including fabrication work at the designated location as instructed by client	100 %	0 %	0 %	100%
Charges for supply of 75mmx 75mm (8mm thick) L angle for 4 DGs	100 %	0 %	0 %	100%
Charges for installation & fabrication of 75mmx 75mm (8mm thick) L angle for 4 DGs	100 %	0 %	0 %	100%
Charges for supply for Epoxy paint for cross bracing	100 %	0 %	0 %	100%
Charges for applying for Epoxy paint for cross bracing	100 %	0 %	0 %	100%
Scaffolding Charges	100 %	0 %	0 %	100%

Project Task Timeline

TASK NAME	12-JUL	13-JUL	14-JUL	TOTAL
Loading/ Unloading Transportation Charges	100 %	0 %	0 %	100%

Project Task Progress Summary

Charges for dismantling, cutting & removing of the existing cross bracing that is obstructing the door

Start: 2026-07-12 | End: 2026-07-14 | Completed

DATE	STATUS (IN %)	REMARKS	IMAGES
2026-07-12	100 %	completed	No Images
2026-07-13	0 %	—	No Images
2026-07-14	0 %	—	No Images

Charges for fixing of existing cut cross bracing including fabrication work at the designated location as instructed by client

Start: 2026-07-12 | End: 2026-07-14 | Completed

DATE	STATUS (IN %)	REMARKS	IMAGES
2026-07-12	100 %	completed	No Images
2026-07-13	0 %	—	No Images
2026-07-14	0 %	—	No Images

Charges for supply of 75mmx 75mm (8mm thick) L angle for 4 DGs

Start: 2026-07-12 | End: 2026-07-14 | Completed

DATE	STATUS (IN %)	REMARKS	IMAGES
2026-07-12	100 %	completed	No Images
2026-07-13	0 %	—	No Images
2026-07-14	0 %	—	No Images

Charges for installation & fabrication of 75mmx 75mm (8mm thick) L angle for 4 DGs

Start: 2026-07-12 | End: 2026-07-14 | Completed

DATE	STATUS (IN %)	REMARKS	IMAGES
2026-07-12	100 %	completed	No Images
2026-07-13	0 %	—	No Images
2026-07-14	0 %	—	No Images

Charges for supply for Epoxy paint for cross bracing

Start: 2026-07-12 | End: 2026-07-14 | Completed

DATE	STATUS (IN %)	REMARKS	IMAGES
2026-07-12	100 %	completed	No Images
2026-07-13	0 %	—	No Images
2026-07-14	0 %	—	No Images

Charges for applying for Epoxy paint for cross bracing

Start: 2026-07-12 | End: 2026-07-14 | Completed

DATE	STATUS (IN %)	REMARKS	IMAGES
2026-07-12	100 %	completed	No Images
2026-07-13	0 %	—	No Images
2026-07-14	0 %	—	No Images

Scaffolding Charges

Start: 2026-07-12 | End: 2026-07-14 | Completed

DATE	STATUS (IN %)	REMARKS	IMAGES
2026-07-12	100 %	completed	No Images
2026-07-13	0 %	—	No Images
2026-07-14	0 %	—	No Images

Loading/ Unloading Transportation Charges

Start: 2026-07-12 | End: 2026-07-14 | Completed

DATE	STATUS (IN %)	REMARKS	IMAGES
2026-07-12	100 %	completed	No Images
2026-07-13	0 %	—	No Images
2026-07-14	0 %	—	No Images
